BEHAN BROS., INC

Aquidneck Center Starbucks

06/14/2022

	Activity Name	Predecessors	Duration (Days)	Successors	Start Date	Finish Date
1	**SEQUENCE #01 - Starbucks**					
2	Exploratory Investigation of Water Main location on SW corner of lot					
3	Seperate site lighting electric feed					
4	Submit Mix Design/Rebar Shop Drawings		1.00	FS+5.00, 10FS+12	11/29/22	11/29/22
5	Mobilize Site	4	6.00	6	11/30/22	12/7/22
6	Site Prep/Strip Site	5	5.00	8, 9	12/8/22	12/14/22
7	Structural Steel Fabrication	4FS+5.00	15.00		12/7/22	12/27/22
8	Excavate Foundation	6	6.00	9FS-5.00, 10	12/15/22	12/22/22
9	Underground Utilities	6, 8FS-5.00	20.00	16	12/16/22	1/12/23
10	Formwork	4FS+12.00, 8	13.00	11	12/23/22	1/10/23
11	Backfill Foundation/SOG Prep	10	5.00	12	1/11/23	1/17/23
12	Erect Steel	11	5.00	13	1/18/23	1/24/23
13	Wood Framing/Sheathing/Roof Line Trim	12	25.00	14, 15	1/25/23	2/28/23
14	Roofing	13	5.00	17	3/1/23	3/7/23
15	Exterior Trim/Exterior Door Install	13	15.00	19	3/1/23	3/21/23
16	Stormwater/StormCrete Infiltration System	9	10.00	22, 23	1/30/23	2/10/23
17	Installation of Exterior Storefront/Service Windows	14	7.00	18, 19	3/8/23	3/16/23
18	MEP In-Wall Rough	17	15.00		3/17/23	4/6/23
19	Exterior Siding	15, 17	10.00	20	3/22/23	4/4/23
20	Exterior Painting	19	3.00	21	4/5/23	4/7/23
21	MEP/FP Finishes - Exterior Lighting	20	5.00		4/10/23	4/14/23
22	Subgrade Prep - Rough Grade	16	4.00	23	2/13/23	2/16/23
23	Exterior Improvments - Curbing and Exterior Concrete	16, 22	20.00	24, 25	2/17/23	3/16/23
24	Exterior Improvments - Asphalt Binder	23	2.00	26FS+5.00	3/17/23	3/20/23
25	Site Furnishings/Signage	23	7.00		3/17/23	3/27/23
26	Exterior Improvments - Topping Course	24FS+5.00	2.00	27	3/28/23	3/29/23
27	Loam/Topsoil and Site Restoration/Fencing	26	7.00	28, 29	3/30/23	4/7/23
28	Site Lighting Finishes	27	4.00		4/10/23	4/13/23
29	Landscaping	27	8.00	30	4/10/23	4/19/23
30	Strip Top Course/Parking Stops	29	2.00		4/20/23	4/21/23
31						
32						
33	**SEQUENCE #02 - Christmas Tree Shop Parking Area**					
34	Mobilize Site		3.00	36	4/10/23	4/12/23
35	P1: WEST Christmas Tree Lot Area		**31.00**		**4/13/23**	**5/25/23**
36	Site Prep/Strip Site	34	3.00	37, 38	4/13/23	4/17/23
37	Pour/Set Transformer Pad	36	3.00	39	4/18/23	4/20/23
38	Trenching & Underground Utilities / Inspection +1D	36	6.00	39, 40	4/18/23	4/25/23
39	NGRID-E Transformer Set	37, 38	5.00	41	4/26/23	5/2/23
40	Set Pole Bases	38	2.00	41	4/26/23	4/27/23
41	Subgrade Prep - Rough Grade	39, 40	4.00	42	5/3/23	5/8/23
42	Exterior Improvements - Curbing	41	4.00	43	5/9/23	5/12/23
43	Fine Grade	42	3.00	44	5/15/23	5/17/23
44	Exterior Improvments - Asphalt Binder	43	2.00	45	5/18/23	5/19/23
45	Exterior Improvments - Topping Course	44	2.00	46	5/22/23	5/23/23
46	Stripe Top Course	45	2.00	48	5/24/23	5/25/23
47	P2: EAST Christmas Tree Lot Area		**27.00**		**5/26/23**	**7/3/23**
48	Site Prep/Strip Site	46	3.00	49	5/26/23	5/30/23
49	Trenching & Underground Utilities	48	4.00	50	5/31/23	6/5/23
50	Set Pole Bases	49	2.00	51	6/6/23	6/7/23
51	Subgrade Prep - Rough Grade	50	3.00	52	6/8/23	6/12/23
52	Exterior Improvements - Curbing	51	6.00	53	6/13/23	6/20/23
53	Fine Grade	52	3.00	54	6/21/23	6/23/23
54	Exterior Improvements - Asphalt Binder	53	2.00	55	6/26/23	6/27/23
55	Exterior Improvements - Topping Course	54	2.00	56	6/28/23	6/29/23
56	Stripe Top Course	55	2.00	58	6/30/23	7/3/23
57	P3: Citizens & Aquidneck Liquors Drivelane		**36.00**		**7/4/23**	**8/22/23**
58	Site Prep/Strip Site	56	2.00	59	7/4/23	7/5/23
59	Trenching & Underground Utilities	58	5.00	60	7/6/23	7/12/23

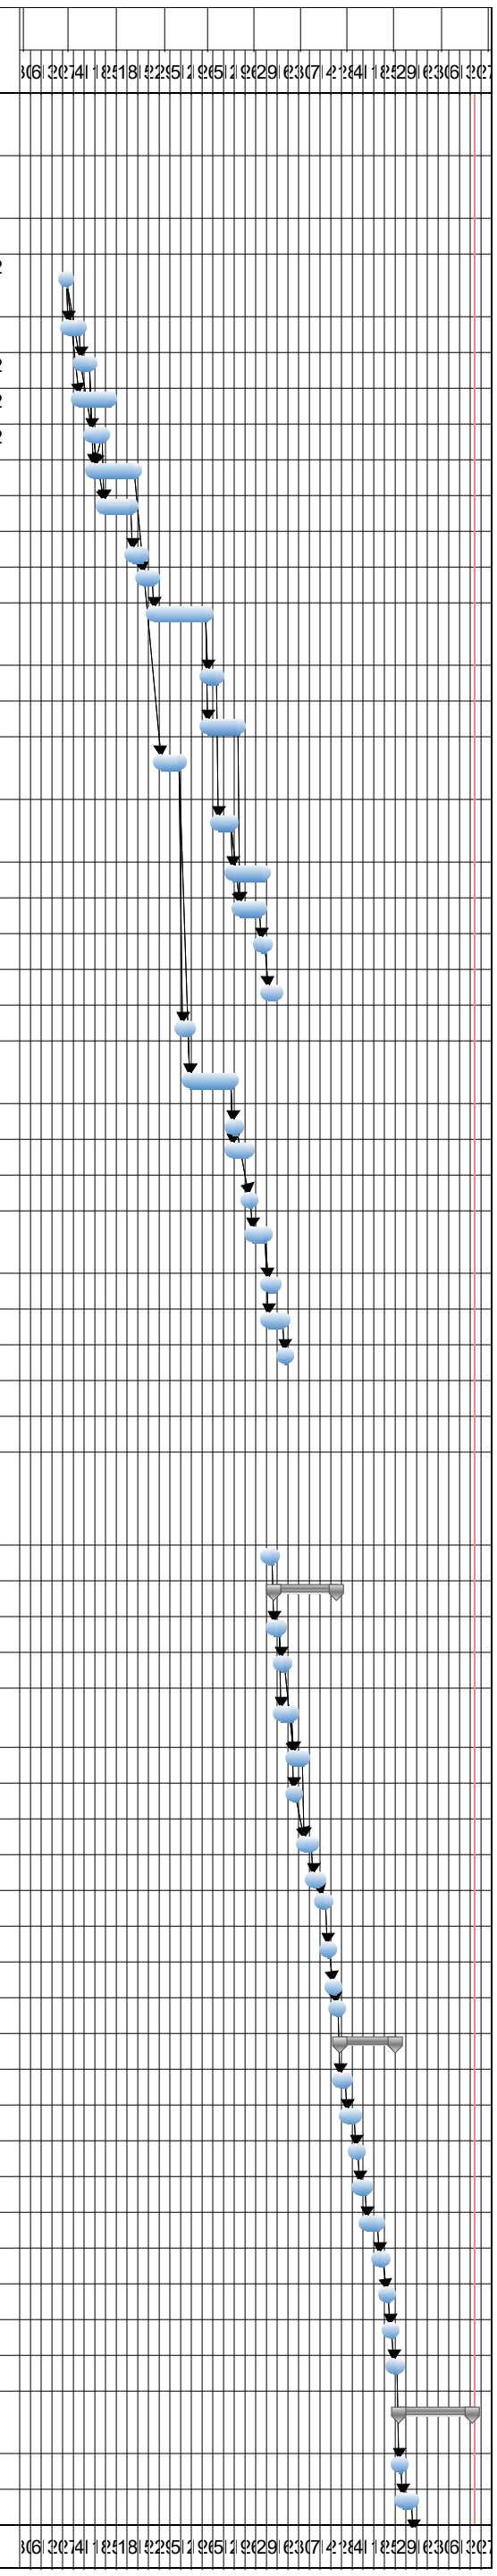

BEHAN BROS., INC

Aquidneck Center Starbucks

03/22/2022
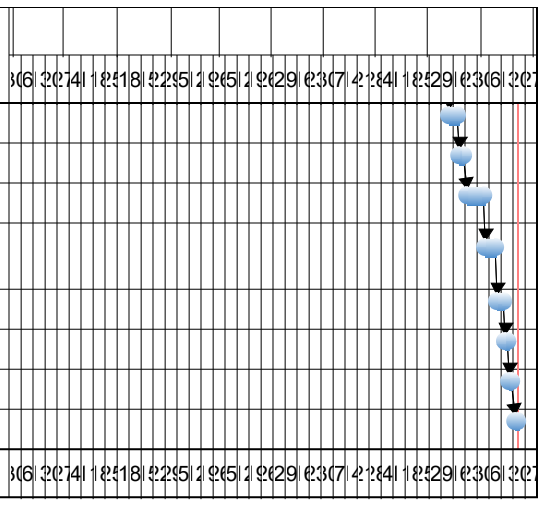
	Activity Name	Predecessors	Duration (Days)	Successors	Start Date	Finish Date
60	Set Pole Bases	59	4.00	61	7/13/23	7/18/23
61	Subgrade Prep - Rough Grade	60	3.00	62	7/19/23	7/21/23
62	Exterior Improvements - Curbing	61	8.00	63	7/24/23	8/2/23
63	Exterior Improvements - Citizens Bank Shut Down - Set curbing, Bollards	62	5.00	64	8/3/23	8/9/23
64	Fine Grade	63	3.00	65	8/10/23	8/14/23
65	Exterior Improvements - Asphalt Binder	64	2.00	66	8/15/23	8/16/23
66	Exterior Improvements - Topping Course	65	2.00	67	8/17/23	8/18/23
67	Stripe Top Course	66	2.00		8/21/23	8/22/23
